Project Execution Plan (PEP)

Prepared For:

Inovo Telecom (Pty) Ltd

Prepared by: E. Gerber

Table of Contents

1 Introduction 3
1.1 Project Purpose 3
1.2 Solution Overview 3
1.2.1 Snaptel Description 3
1.2.2 System Organization 3
2. Project Objectives 4
2.1 Project Goals 4
2.2 Success Measures 4
2.3 Assumptions and Constraints 4
2.4 SWOT Analysis 5
3. Stakeholder Assessment and Management Plan 6
3.1 Stakeholder Assessment 6
3.2 Inovo Project Stakeholder Matrix 6
3.3 Stakeholder Communication Summary 7
4. Project Workstream Mapping. 8
5. Critical Path 9
6. Decision Making Framework & Contact Information 10
ANNEXURE A: High-Level Solution Diagram 11
ANNEXURE B: Softphone Solution Work Breakdown Structure (WBS) 12
ANNEXURE C: Softphone Critical Path (Go-Live to Project Closure) 13
ANNEXURE D: Project DACI Matrix & Directory 14

1 Introduction

1.1 Project Purpose

Inovo Telecom is currently exploring opportunities to enhance their communication capabilities. By deploying a proprietary, scalable Vodia Snaptel solution, Inovo will reduce variable costs, increase client retention through deep workflow integration, and offer a specialized, accessible solution that differentiates them in the South African corporate market.

1.2 Solution Overview

1.2.1 Snaptel Description

Snaptel is an enterprise-grade platform designed for high scalability and business intelligence.

Core Architecture: Built on the Vodia PBX stack, optimized for multi-tenancy and high-density environments.

Omnichannel Access: Users connect via Desktop, Mobile App, or hardware devices such as desk phones.

AI Integration: Includes "Coming Soon" features like AI Sentiment Analysis and native South African voice-powered virtual agents.

Management: The **Snaptel Orchestrator** provides a single pane for Inovo to monitor infrastructure and manage user extensions with minimal variable cost.

1.2.2 System Organization

Following the High-Level Solution Diagram **[Annexure A]**, the architecture is designed for "Zero Downtime" through geographic redundancy.

- **Dual Hubs:** The Snaptel solution is split between Teraco Isando (JB1) and Teraco Rondebosch (CTI).
- **Redundancy:** Each site hosts a high-availability Cluster and a dedicated Session Border Controller (SBC).
- **Connectivity:** 1 Gbps Fibre connects the sites, ensuring sub-30ms latency for voice traffic. This may be upgraded to 10Gbps in future and if requested by the client.
- **Storage:** All call recordings can be securely offloaded to client storage for long-term compliance and retrieval.
- **End-Points:** The architecture supports a "Work from Anywhere" model, bridging the Client LAN (Desk phones) with the public internet (Mobile/Desktop clients) through encrypted tunnels.

2. Project Objectives

2.1 Project Goals

To successfully implement a dual-site, high-availability IP PBX Vodia Snaptel solution supporting up-to 15,000 extensions, achieving 99.9% system uptime and 100% accessibility compliance for specialized operators by September 30, 2026. The Snaptel solution design allows INOVO to scale beyond the initial committed extension quantity. The solution will support JAWS integration and provide accessibility to specialized operators.

2.2 Success Measures

Project Key Performance Indicators (KPI) Measures:

- **System Uptime**: Minimum 99.9% uptime during the migration and stabilization phases.
- **Accessibility Success**: 100% of JAWS-required commands functional for operators.
- **Migration Accuracy**: Zero data loss during extension and profile mapping.
- **Training Completion**: > 95% of trainers, trained before their specific site installation and "Go-Live" planned date.
- **User Adoption**: User training, supporting documentation and training materials
- **Migration Velocity**: Maintaining a planned rate of migrations per week to meet the September deadline.

2.3 Assumptions and Constraints

PROJECT ASSUMPTIONS	
PBX Routing	PBX will route al traffic to Inovo supplied SBS's.
Installations	Inovo will be responsible for all field services and site installations, apart from the two complimentary installations provided by ICTGlobe.
Authority (SSO)	It is assumed that Inovo or the end-client's IT Global Administrators will provide the necessary "Admin Consent" and API permissions within their MS Entra ID tenants to allow for multi-tenant authentication and automated user provisioning.
Data Integrity	The project assumes that the divisional data provided in the *Inovo Business Units* master sheets will be accurate and current. The technical configuration is entirely dependent on this data being 100% true.
Support	Per the SLA, it is assumed that Inovo maintains a fully functional internal helpdesk capable of handling all end-user troubleshooting (Level 1) and hardware-related issues, as ICTGlobe's responsibility is limited to system-level infrastructure (Level 2/3).

PROJECT CONSTRAINTS	
Bandwidth	Bandwidth quality at the end-client site may vary by province; SD-WAN or dedicated Voice VLANs may be required.
Geographic Redundancy	The high-availability (HA) model is strictly constrained by the physical connectivity between Teraco JB1 (Isando) and Teraco CTI (Rondebosch). Any widespread outage affecting the 1Gbps cross-connects between these hubs remains a critical path dependency.
Migration Timelines	The project is constrained by a hard completion date of September 30, 2026. Any delays in regional site surveys or hardware procurement will directly compress the "Stabilization" phase.
Dialling Logic	Due to the enterprise corporate structure, the dial plan is constrained by potential extension overlaps. Strict planning and management of unique extension ranges must be enforced across all users to prevent internal routing conflicts.
Regulatory & Compliance	All voice recording and data storage must strictly comply with POPIA (South Africa) and ICASA regulations. This constrains how and where call data is processed and who has "Manager Access" to recordings within the Snaptel Orchestrator.

2.4 SWOT Analysis

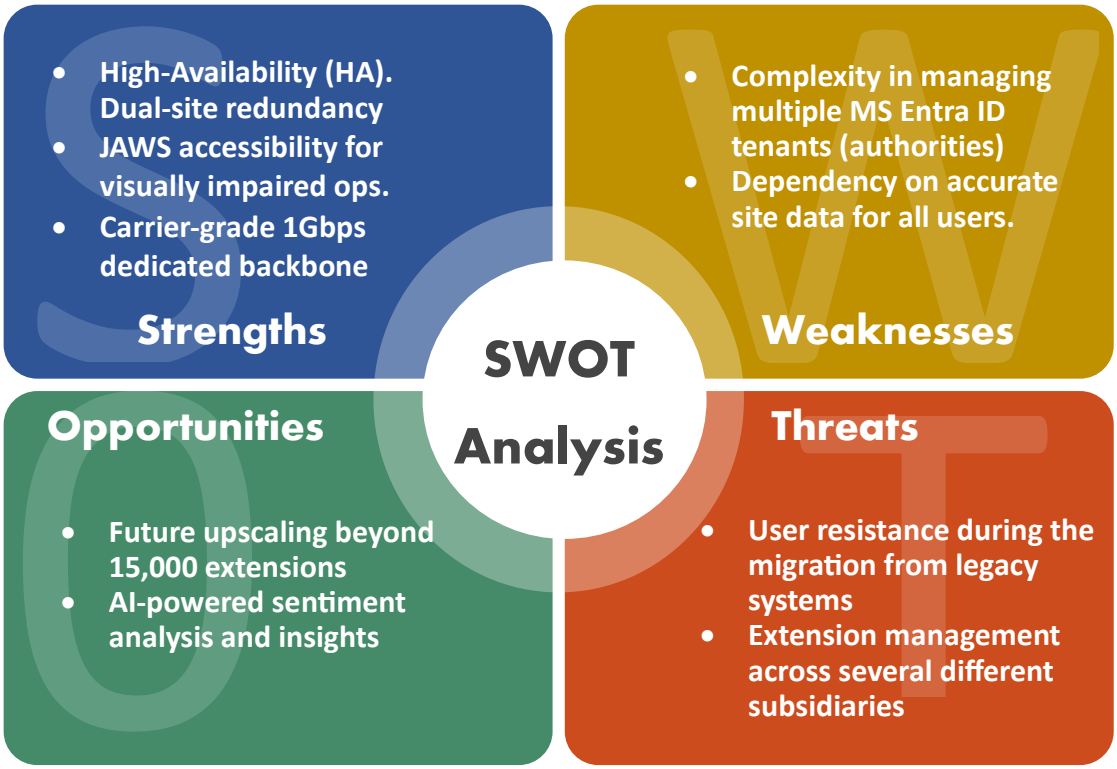

3. Stakeholder Assessment and Management Plan

3.1 Stakeholder Assessment

This stakeholder assessment categorizes stakeholders by their ability to impact the project (Power) and their level of concern regarding project outcomes (Interest).

Stakeholder Group	Classification	Key Concerns & Requirements
The Customer	High Power High Interest	The ultimate entity making use of the solution.
Executives	High Power High Interest	Strategic alignment, ROI, and ensuring the solution meets long-term business goals.
Project Team	High Power Low Interest	End-to-end execution, system stability and project execution.
Technical Leads	High Power Low Interest	Solution design testing and meeting technical milestones.
Technical Engineers	High Power Low Interest	Testing, configuration and implementation of hardware, ensuring site-level performance**.**
Regulatory Bodies (ICASA/POPIA)	High Power Low Interest	Ensuring call recordings (Amazon S3) and data handling comply with South African law.
Company Subsidiaries	Low Power High Interest	"Change Management" newsletters; FAQ, supporting documents, user guides and training.
End-Clients	Low Power Low Interest	Updates as required by compliance or legal workstreams.

3.2 Inovo Project Stakeholder Matrix

Stakeholder	Power	Interest	Influence	Impact	Urgency	Legitimacy	Total Score	Priority
*The Customer	5	5	5	5	5	5	30	Critical
Executives	4	5	5	5	5	5	29	Critical
Project Team	4	5	4	4	4	4	25	High
Technical Leads	4	4	4	4	4	5	25	High
Technical Staff	3	4	3	3	4	3	20	High
Regulatory Bodies	4	2	3	5	3	3	20	High
Subsidiaries	2	4	3	3	3	3	18	Medium
End-Clients	2	2	2	2	2	3	13	Low

3.3 Stakeholder Communication Summary

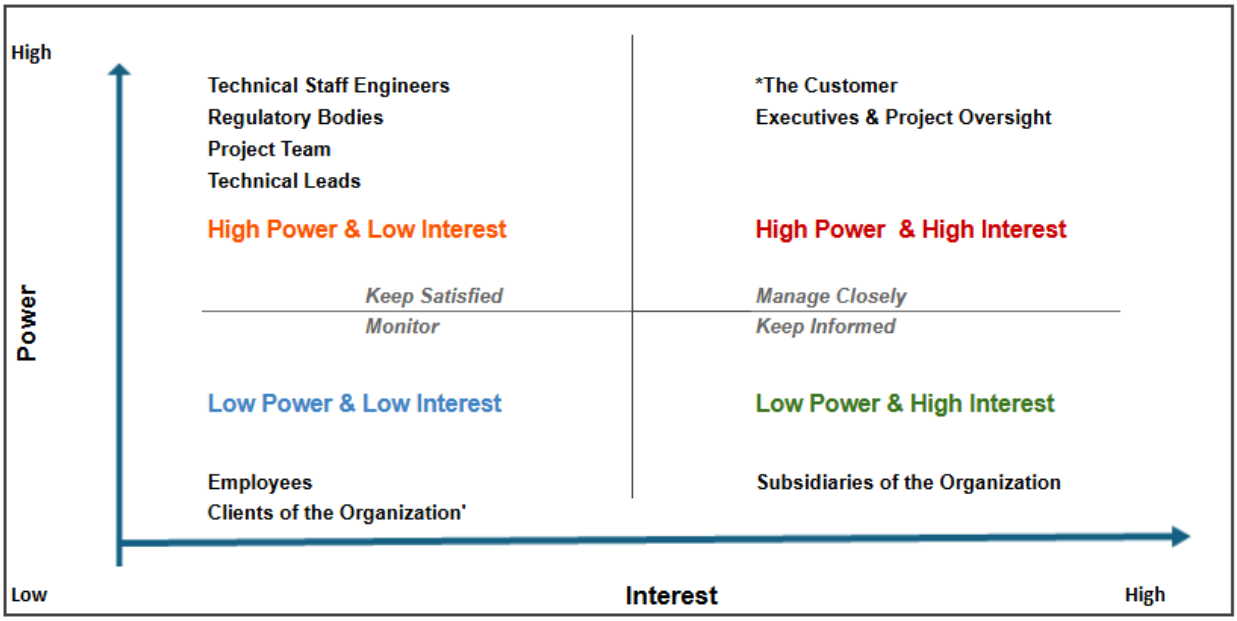

Communication Strategy

Group	Frequency	Method	Primary Goal
High Power High Interest	Monthly	High-level progress reports	Strategic Alignment & Sing-Off
High Power Low Interest	Weekly	Operations Meeting	Technical Execution & SNAG tracking
Low Power High Interest	Fortnightly	Stand-Ups / Email Notifications **Customer Dependant*	"Change Management" newsletters; FAQ, supporting documents.
Low Power Low Interest	Periodic	Stand-Ups / Email Notifications **Customer Dependant*	Periodic updates as required

4. Project Workstream Mapping.

The following workstream mapping provides a structured overview of the functional and technical activities required to deliver the ICTGlobe Softphone solution. These workstreams are designed to ensure seamless integration between Vodia/Snaptel technology and existing enterprise infrastructure while maintaining a primary focus on high availability, regulatory compliance, and specialized accessibility requirements. Each phase outlines specific deliverables and dependencies that align with the project's strategic objective of modernizing communication across diverse business units.

Workstream 1: Infrastructure & Connectivity

This workstream focuses on the physical and network readiness required to host the enterprise voice solution.

- **Cross-Connect Provisioning:** Establishing dedicated connectivity between JB1 and CTI data centres.
- **High Availability (HA) Configuration:** Implementation of redundant Fibre paths and SBC (Session Border Controller) HA clusters to ensure service continuity.
- **Call Recording Storage:** Establishing the AWS S3 recording archiving environment and playback retrieval protocols.

**Requires credentials to store the data on the client's storage.*

Workstream 2: Software Development & System Integration

This workstream manages the customization of the Vodia/Snaptel interface and integration with existing enterprise tools.

- **Vodia/Snaptel Interface Development:** Customizing the softphone application to meet Switchboard, Executive/Secretary, and Trader role requirements.
- **Technical Scope & MS Teams Integration:** Finalizing the technical parameters for MS Teams integration via the Vodia solution.
- **Specialized Function Testing:** Development and testing of additional functionality, Call Preview panels, and Attendant Console features (e.g., split swap, recall, and park).
- **Accessibility Compliance (JAWS):** Execution of Internal JAWS interoperability testing to ensure the softphone supports visually impaired users.

Workstream 3: Organizational Data & Configuration

This workstream governs the mapping of personnel and business units into the new telephony architecture.

- **Business Unit (BU) Mapping**: Structuring the directory for different entities, including Sanlam, Assupol, and Afrocentric, as well as their respective sub-units.
- **Extension & Call Flow Mapping**: Finalizing the 11-digit Dial Plan and global directory access for regional office transfers.
- **Hardware Audit**: Comparative analysis and procurement of Fanvil hardware devices versus legacy equipment.
- **Regional Rollout Coordination**: Sequential deployment of services across designated geographical regions.

Workstream 4: Implementation, Training & UAT

The final phase focuses on user readiness, site-specific setup, and formal acceptance.

- **Pilot Site Setup**: Deployment of the initial pilot site with a performance target of 99.99% uptime.
- **Technical Product Training**: Specialized training for First Line Support and User Configuration administrators.
- **User Acceptance Testing (UAT)**: Formalized testing cycles to ensure all functional requirements (Speed Dial, Call Pickup Groups, Intercom) are met before Go-Live.

Please refer to **Annexure B**: Snaptel Solution WBS (Systems, Infrastructure & Accessibility) for the visual representation of these dependencies.

5. Critical Path

The critical path for this deployment, as can be viewed in **Annexure C**, is driven by the successful migration of users across regional business units, which provides the necessary load to validate the underlying high-availability infrastructure.

- **Pilot Phase**: The path begins with the Pilot Go-Live, which establishes the baseline for Entra ID authentication and the 11-digit dial plan.
- **Parallel Migration**: Upon pilot success, the project splits into parallel regional rollout threads for various client subsidiaries.
- **Infrastructure Dependency**: These regional rollouts are strict dependencies for System Hardening; without the live traffic from these units, the SBC High Availability (HA) clusters and 10Gbps Fibre backhaul cannot be stress-tested for 99.99% uptime.
- **Compliance Convergence**: The final technical milestone is the validation of the recording archives, ensuring all legal and regulatory data is correctly captured across all units.
- **Final Installation**: The path concludes at the Final Site Installation, representing the completion of software and/or hardware deployment and the formal project closure.

6. Decision Making Framework & Contact Information

Based on this project's stakeholder management plan and the technical requirements outlined in the solution design, the following demonstrates the **DACI (Driver, Approver, Contributor, Informed)** matrix for the Inovo Snaptel project.

This matrix clarifies who is responsible for execution, who has the final sign-off, who provides expert input, and who is kept in the loop regarding project progress.

Role	Responsibility	Personnel
Driver (D)	Direct project path to ensure success for everyone involved	Estelle Gerber Oscar Miles
Approver (A)	Offers non-biased, objective approach to project tasks and decisions	Hannes Viljoen Eugene Strydom Wynand Smit Jan Kuhn The Client
Contributor (C)	Executes project decisions and tasks based in their knowledge or experience.	Gregorio Fernandes Jolene Geyser Lucien Brink ICTGlobe Developers Quintin Myburgh Jaques Pyper Bheki Mhlanga Sibusiso Ngcobo
Informed (I)	Stakeholders with no direct involvement with the project.	Employees of the business Subsidiaries of the organization Adjacent business units Adjacent departments End users receiving the final deliverable

Please refer to **Annexure D**: Project DACI Matrix & Directory, outlining the project's responsibility assignment matrix.

ANNEXURE A: High-Level Solution Diagram

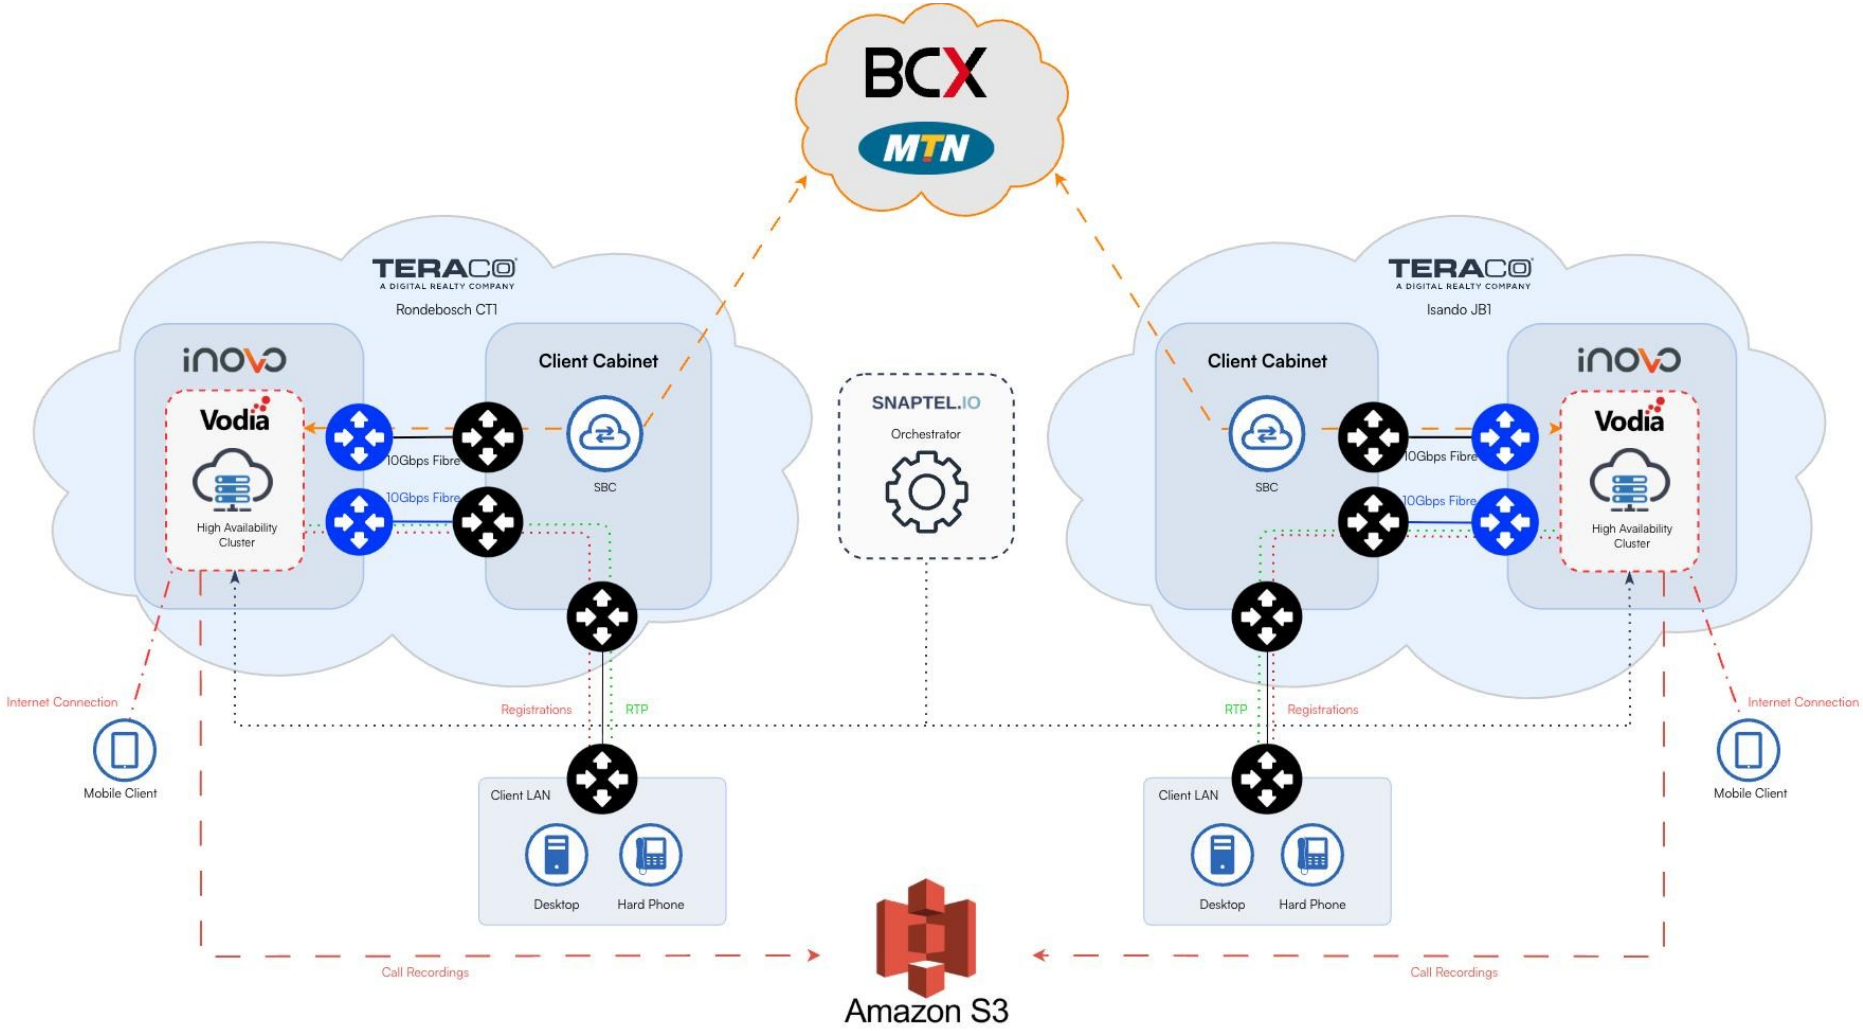

ictglobe

ANNEXURE B: Softphone Solution Work Breakdown Structure (WBS)

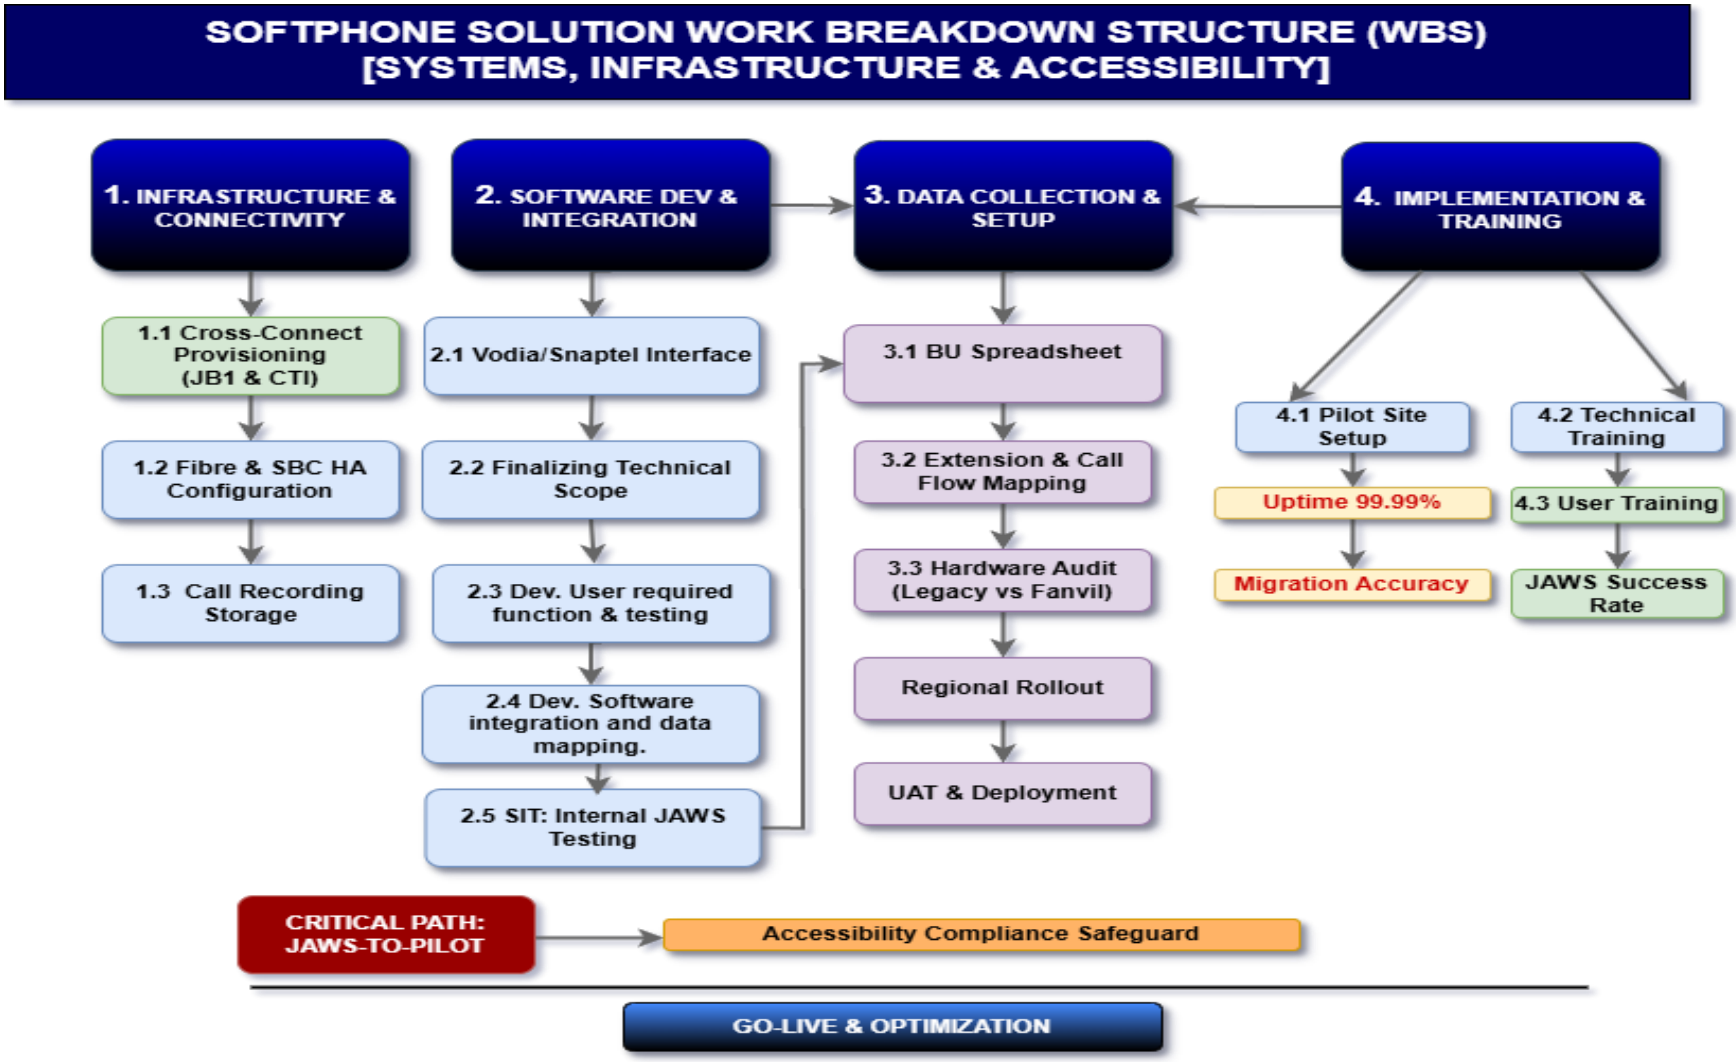

ictglobe

ANNEXURE C: Softphone Critical Path (Go-Live to Project Closure)

ANNEXURE B: SOFTPHONE CRITICAL PATH (GO-LIVE TO PROJECT CLOSURE)

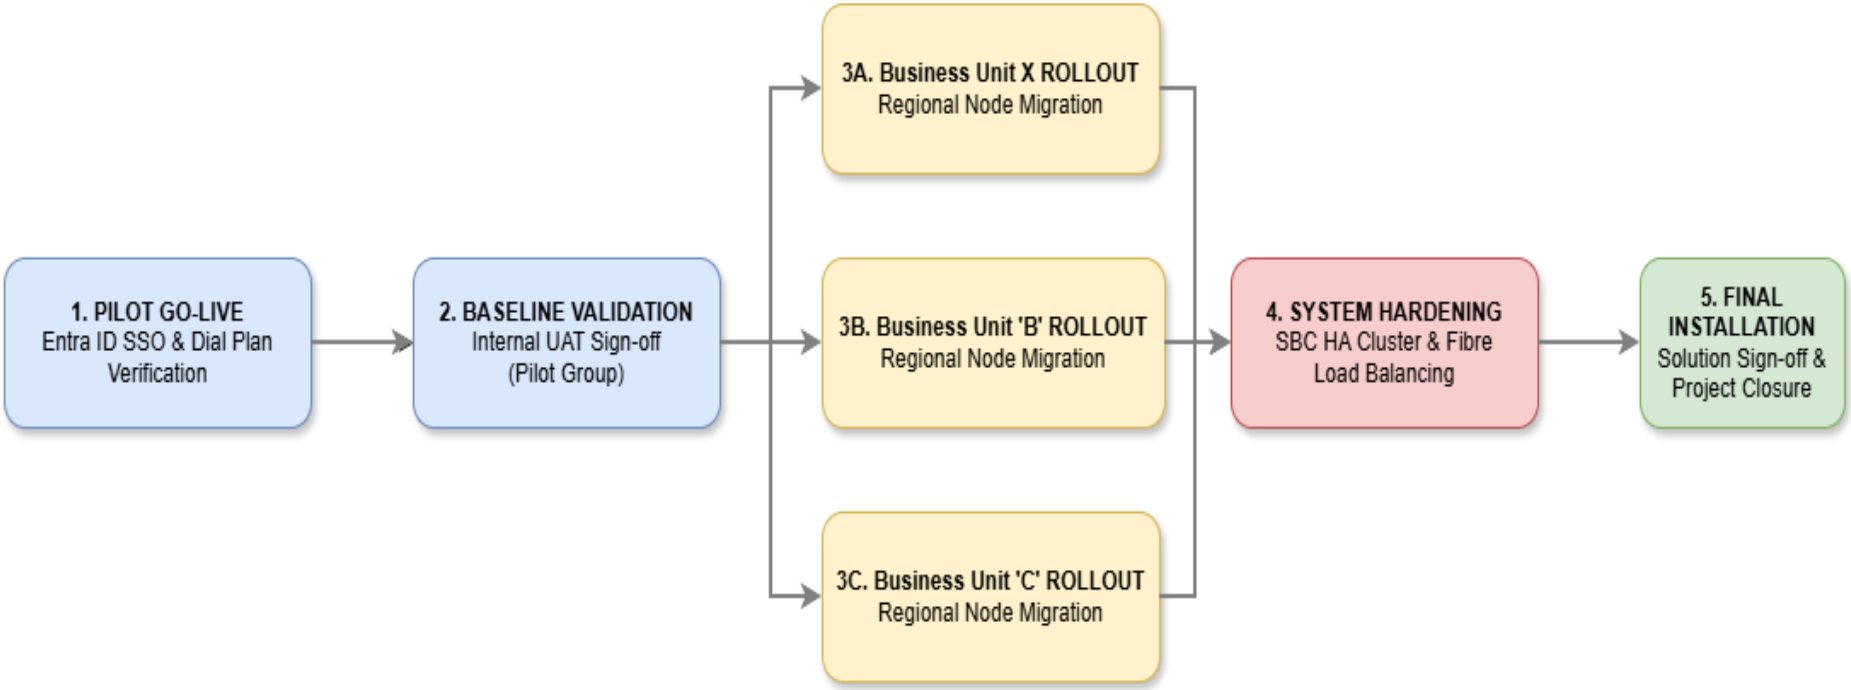

Note: Parallel Regional Rollouts (3A, 3B, 3C) are the primary drivers for System Hardening load testing.

ANNEXURE D: Project DACI Matrix & Directory

PROJECT DACI MATRIX & DIRECTORY

DACI ASSIGNMENTS

DRIVER (D)
Estelle Gerber
Oscar Miles

APPROVER (A)
Hanes Viljoen
Eugene Strydom
Wynand Smit
Jan Kuhn
The Client

CONTRIBUTOR (C)
Jolene Geyser,
Gregorio Fernandes
Lucien Brink
Craig Green
Joe Joubert
Quintin Myburgh
Jaques Pypers
Bheki Mhlanga
Sibusiso Ngcobo

INFORMED (I)
Employees of the Business
Subsidiaries of the organization
Adjacent Departments
End Users of Snaptel

CORE RESPONSIBILITES

- Establish & ensure project deliverables
- Assign individual tasks & activities
- Set goals, milestones and deadlines
- Organizing and running meetings
- Maintaining project documentation

- Final say on project details or tasks

- Business and data analysts
- Industry and subject matter experts
- Product designers and engineers
- Customer support and sales representatives
- Product or service client
- Business owner and investors

- No direct authority with decision making
- Keep track of project progress

CONTACT DIRECTORY

NAME	EMAIL
Estelle Gerber	estelle@ictglobe.com
Oscar Miles	oscar.miles@inovo.co.za
Eugene Strydom	eugene.strydom@ictglobe.com
Wynand Smit	wsmit@inovo.co.za
Jan Kuhn	jkuhn@inovo.co.za
Jolene Geyser	jolene.geyser@ictglobe.com
Gregorio Fernandes	gf@ictnetworks.co.za
Lucien Brink	lucien.brink@ictglobe.com
Craig Green	craig.green@ictglobe.com
Joe Joubert	joe.joubert@ictglobe.com
Quintin Myburgh	qmyburgh@inovo.co.za
Jaques Pyper	jpypers@inovo.co.za
Bheki Mhlanga	bmhlanga@inovo.co.za
Sibusiso Ngcobo	sngcobo@inovo.co.za
